


Level 2 Project Management (7574-226)

ITQ (QCF)
Assignment guide for Candidates
Assignment B

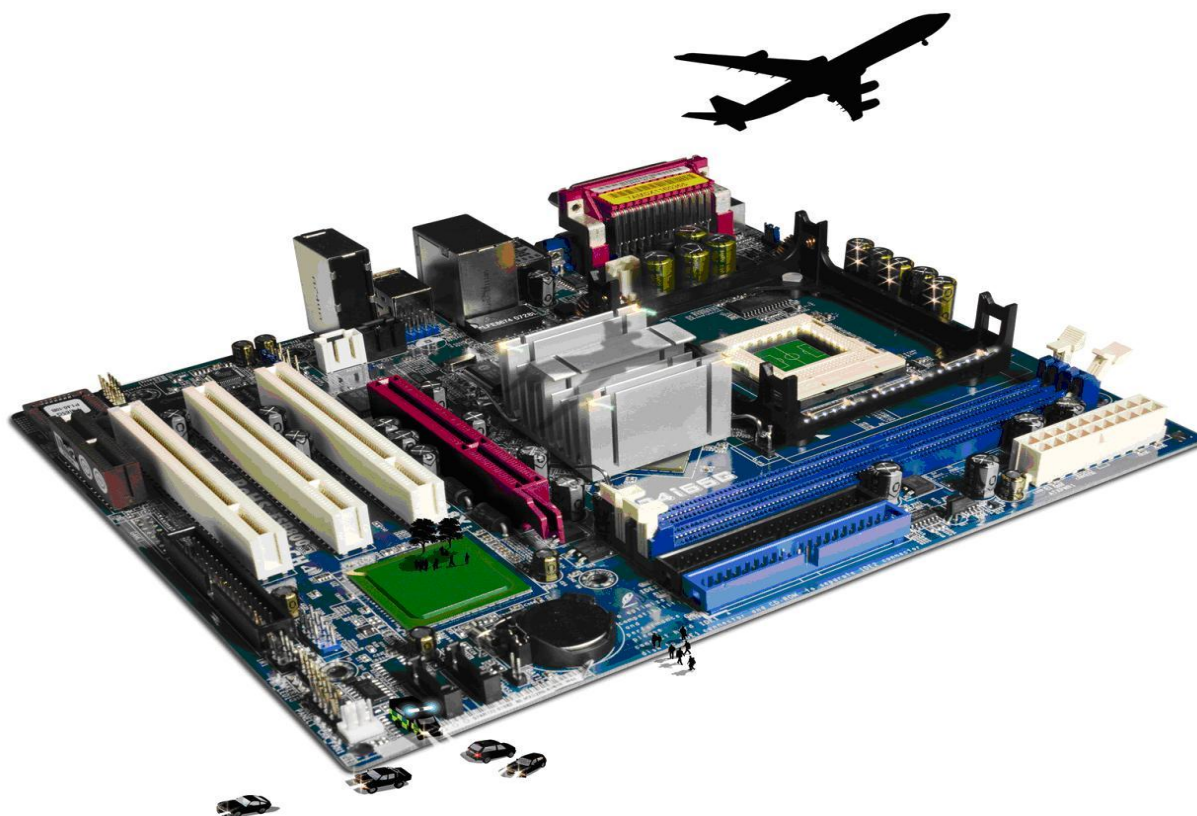

About City & Guilds

City & Guilds is the UK's leading provider of vocational qualifications, offering over 500 awards across a wide range of industries, and progressing from entry level to the highest levels of professional achievement. With over 8500 centres in 100 countries, City & Guilds is recognised by employers worldwide for providing qualifications that offer proof of the skills they need to get the job done.

City & Guilds Group

The City & Guilds Group includes City & Guilds, ILM (the Institute of Leadership & Management) which provides management qualifications, learning materials and membership services, NPTC which offers land-based qualifications and membership services, and HAB (the Hospitality Awarding Body). City & Guilds also manages the Engineering Council Examinations on behalf of the Engineering Council.

Equal opportunities

City & Guilds fully supports the principle of equal opportunities and we are committed to satisfying this principle in all our activities and published material. A copy of our equal opportunities policy statement is available on the City & Guilds website.

Copyright

The content of this document is, unless otherwise indicated, © The City and Guilds of London Institute 2010 and may not be copied, reproduced or distributed without prior written consent.

However, approved City & Guilds centres and learners studying for City & Guilds qualifications may photocopy this document free of charge and/or include a locked PDF version of it on centre intranets on the following conditions:

- centre staff may copy the material only for the purpose of teaching learners working towards a City & Guilds qualification, or for internal administration purposes
- learners may copy the material only for their own use when working towards a City & Guilds qualification

The *Standard Copying Conditions* on the City & Guilds website also apply.

Please note: National Occupational Standards are not © The City and Guilds of London Institute. Please check the conditions upon which they may be copied with the relevant Sector Skills Council.

Publications

City & Guilds publications are available on the City & Guilds website or from our Publications Sales department at the address below or by telephoning +44 (0)20 7294 2850 or faxing +44 (0)20 7294 3387.

Every effort has been made to ensure that the information contained in this publication is true and correct at the time of going to press. However, City & Guilds' products and services are subject to continuous development and improvement and the right is reserved to change products and services from time to time. City & Guilds cannot accept liability for loss or damage arising from the use of information in this publication.

City & Guilds

1 Giltspur Street

London EC1A 9DD

T +44 (0)844 543 0000 (Centres)

T +44 (0)844 543 0033 (Learners)

www.cityandguilds.com

learnersupport@cityandguilds.com

Contents

Unit 226 – Project Management Level 2

Assignment B

Introduction – Information for Candidates	2
Candidate instructions	3

Level 2 Project Management (7574-226)

Assignment B

Introduction – Information for Candidates

About this document

This assignment comprises all of the assessment for Level 2 Project Management (7574-226).

Health and safety

You are responsible for maintaining the safety of others as well as your own. You are asked to work safely at all times.

You will **not** be allowed to continue with an assignment if you compromise any of the Health and Safety requirements.

Time allowance

The recommended time allowance for this assignment is **two hours**.

Level 2 Project Management (7574-226)

Candidate instructions

Time allowance: Two hours

The assignment:

This assignment is made up of **four** tasks

- Task A - File set up
- Task B - Document layout
- Task C - Further document layout
- Task D - File update

Scenario

At a recent club meeting you agreed to help with the management of a new games room project. The secretary of the club has sent you an email which contains all the information you need to set the project up using ICT.

Read all of the instructions carefully and complete the tasks in the order given.

Task A – File set up

- 1 Open software that is suitable for project planning.
- 2 Read the Music Project Brief you have been given and set your **PROJECT END**.
- 3 Give your project a heading and save the file using an appropriate file name and any other information you have been given.
- 4 Add **Mr Reiden** as manager of the project to the Project Information.
- 5 Use the brief to identify the **critical project information** and note this in your Planning Document.
- 6 Use the brief to identify the **critical tasks** and any **milestones** and people responsible for each task.

Note this down in your Planning Document.

- 7 Use the information you have identified to draw up a PERT analysis to estimate the time required for each task. Show dependencies on the analysis, use the Planning Document for this.

- 8 Identify **three** risks and issues that may have an impact on the project and note these in the Planning Doc.

Task B – Document layout

- 1 Use the information from the analysis to set all tasks and milestone dates.
- 2 Add the person responsible for each task/activity to the plan.
- 3 Add Installation Engineers as a Cost Resource and assign them as required.
- 4 Link all dependencies as per your **Planning Document**.
- 5 Print/screenprint a copy of the Network Diagram or similar chart to show all tasks, dates, resources and dependencies.
- 6 Add a milestone to indicate that the floor and sound system should be completed by the date you have identified in your **PERT** analysis.
- 7 Add a milestone to indicate the date that the sound proofing should be completed.
- 8 Add a milestone to indicate the date when the recording system should be set up.
- 9 Add a milestone to indicate the date and time of the visit.
- 10 Printout/screenprint a copy of the plan as a **GANTT CHART**.
- 11 Printout/screenprint a **RESOURCE USAGE** report showing everyone's tasks and progress so far.
- 12 Save the project file with the same name.

Task C – Further document layout

- 1 Set the working day in the calendar to start at 9 am and finish at 5 pm. Lunch is between 1pm and 2pm.
- 2 Create a **MUSIC ROOM** calendar and add the days that the Music Theatre is available for installations.
- 3 Take a screen print (or printout) of the MUSIC ROOM showing availability for installations and paste it into your Document Planning file.

- 4 The floor is going to be laid down **two** days later than first noted – update the plan to show the change.
- 5 Show the Recording System set up as 75% complete.
- 6 You have received a copy of the Marketing Plan – record this as complete.
- 7 Re print the **Network Diagram** showing all updates.

Task D – File update

- 1 Print/screenprint a report showing the progress of the project (this **MUST** show the percentage of tasks complete as well as those started or not started).
- 2 Print/screenprint a report that shows resource usage.
- 3 Save the report as “**activityyourname**” (don’t forget any specific naming requests).
- 4 Add the number 2 to the original file name and save “**name2**” (don’t forget any specific naming requests).
- 5 Close the project management software.

When you have finished working:

- Sign each document above your name and label all removable storage media with your name.
- Hand all paperwork and removable storage media to your assessor.

If the assignment is taken over more than one period, all paperwork and removable media must be returned to the test supervisor at the end of each sitting.

End of assignment

Published by City & Guilds
1 Giltspur Street
London
EC1A 9DD
T +44 (0)844 543 0000 (Centres)
T +44 (0)844 543 0033 (Learners)
www.cityandguilds.com

**City & Guilds is a registered charity
established to promote education
and training**
